2018-19

THIRD PARTY INSPECTION REPORT

Name of the Client : **Executive Engineer,**
Electrical- Yelahanka Division,
BBMP, Bangalore.

Name of Agency : **Executive Engineer-1,**
KRIDL, Bangalore.

Name of the Work : Providing Street Lights and Electrical accessories in Ward No.06 , BBMP, Bangalore.

Estimated Cost - Rs. 50.00 Lakhs

THIRD PARTY INSPECTION CONSULTANTS

CIVIL QUALITY CONSULTANTS AND ENGINEERS
NABL Accredited as per ISO/IEC: 17025-2005 Laboratory
An ISO 9001 2008 Certified Company

#133, Bhuvaneshwarinagar, Dodda Basti Main Road, Bangalore-560056
e-mail: civilqualityconsultants@gmail.com Ph: 8553518550/9886998316

"TheRoadtoSuccessisalwaysunderConstruction"

Executive Engineer
Electrical Division
Yelahanka Zone BBMP
Byatarayanapura, Bangalore-92

CIVIL QUALITY CONSULTANTS & ENGINEERS

(Buildings Geo-Tech & Highway Materials Testing Laboratory)
An ISO 9001: 2015 Certified Company
NABL Accredited As Per ISO/IEC : 17025:2005 Laboratory

NO: CQCE/3rd Party/E-Yelahanka Division/06/ 2018-19 Date: 29.11.2018

To,
Executive Engineer,
Elctrical –Yelahanka Division
BBMP, Bangalore.

Sir

Sub:- Submission of 3rd Part Report for the work of Providing Street Lights and Electrical accessories in Ward No.06 , BBMP, Bangalore.reg.

Ref:- (i) Work order No. EE(Elec)/YZ/WO/000014/2018-19 Dated: 21.07.2018
(ii)**Job code No**. 06-18-000028

Adverting to the above, we would like to submit the 3rd Part Inspection Report for the above said work in Electrical - Yelahanka Division along with Mr. Rajendra Nayak (Assistant Executive Engineer, Electrical Yelahanka Zone), and Mr. Kumar (Electrtical Engineer, 3rd Party Consultants), Bangalore on 28.11.2018

The following works inspected the details of works inspected is as follows,

Sl no	Name of the work	Amount of estimate Rs in Lakhs.	Remarks
1	Providing Street Lights and Electrical accessories in Ward No.06 , BBMP, Bangalore.	Rs. 50.00 Lakhs (1st and Final bill)	Work carried out satisfactorily Details mentioned in 3rd party compliance report

For details of works and measurements checked during the inspection time in the presence if the officials /officers afore said.

This is for favor of kind information and needful in the matter.

Enclosures: 3rd part Inspection report
Thanking you

Yours faithfully
Authorized signatory

Executive Engineer
Electrical Division
Yelahanka Zone BBMP
Byatarayanapura, Bangalore-92

Office & Laboratory : # 133, Bhuvaneshwarinagar, Dodda Basti Main Road, Bangalore - 560 056.
e-mail:civilqualityconsultants@gmail.com Ph: 080-23240644 / Mob: 8553518550

Name of Work : Providing Street Lights and Electrical accessories in Ward No.06 , BBMP, Bangalore.

Contractor/Agency	:	**Executive Engineer-1**, KRIDL, Bangalore.
Name of Client	:	**Executive Engineer,** Electrical-Yelahanka Division, BBMP, Bangalore.
Total Bill Cost in Lakhs	:	Rs.49.98 Lakhs
Date Of Inspection	:	28.11.2018
Status of Bill	:	First & Final Bill
In the Presence of	:	(a) **Mr. Rajendra Nayak (Assitant Executive Engineer, Electrical Yelahanka Zone),** BBMP, Bangalore.
	:	(b) **Mr. kumar,** (Electrical Engineer) M/s Civil Quality Consultants & Engineers, Bangalore.

3rd Party Compliance Report

Sl. No	Description of the Item	Unit	Quantity	Comments / observations
1	LED street light supply of LED Streetlight with pressure die cast aliminum housing body with optimal heat sink.....	Each	214	Supplied Material Quality found satisfactory
	27/4.36 1)90 Watts			
2	Supplying and fixing of 32 mm dia class A GI pipe bracket upto 2mtrs long bent at suitable angle	Each	204	Supplied Material Quality found satisfactory
3	Wiring for lighting/power circuit using one of PVC insulated 1100V grade,multistrand copper	P/Mtr	497	Supplied Material Quality found satisfactory
4	supplying of LT UG Cable having aluminum conductor PVC insulated,sheathed.....	P/Mtr	149	Supplied Material Quality found satisfactory
5	labour charges for laying of 1.1KV class UG cable when supplied.....	P/Mtr	149	Supplied Material Quality found satisfactory

CIVIL QUALITY CONSULTANTS & ENGINEERS Bangalore

6	Supplying and fixing angle iron frame work fabricated out of M.S flat... With bolts.....	Mtr	10	Supplied Material Quality found satisfactory
7	Supplying and stringing of ACSR Conductor	P/Mtr	2985	Supplied Material Quality found satisfactory
8	1.1 KV Pin insulator	Each	50	Supplied Material Quality found satisfactory
9	No.8 Strain Insulator	Each	75	Supplied Material Quality found satisfactory
10	2 Pin 45x45x5mm -510mm	Each	109	Supplied Material Quality found satisfactory
11	Fixing halogen / metal halide / SVL / IL LED floodlight fitting over Existing pole.....	Each	98	Supplied Material Quality found satisfactory
12	Supply and installation / fixing / Provision of pole box with HRC fuse / MCB Provision and	Each	22	Supplied Material Quality found satisfactory
13	Supplying and fixing MCCB over the existing wood/Panel board using necessary screws.....	Each	22	Supplied Material Quality found satisfactory
14	Supplying tinned copper lugs and crimping and wiring to terminal point for wire.....	Each	98	Supplied Material Quality found satisfactory

Verified By

CIVIL QUALITY CONSULTANTS & ENGINEERS Bangalore

Authorised Signatory

For CIVIL QUALITY CONSULTANTS & ENGINEERS

Authorised Signatory

Providing Street Lights and Electrical accessories in Ward No.06 , BBMP, Bangalore.

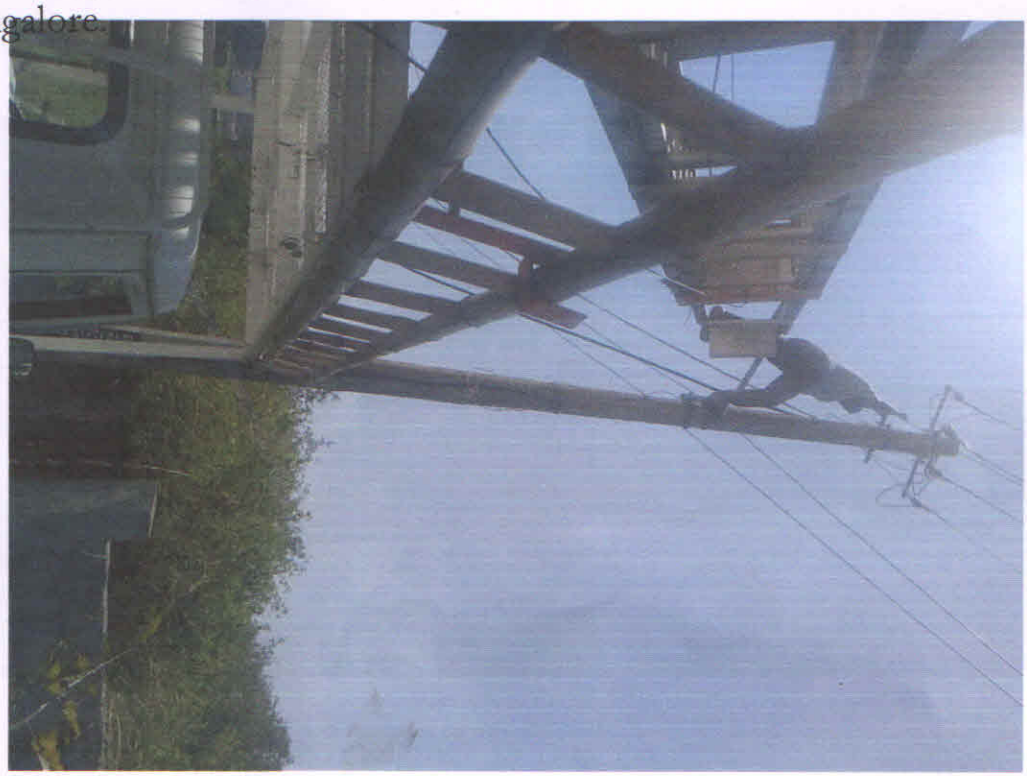

CIVIL QUALITY CONSULTANTS & ENGINEERS
Bangalore

Providing Street Lights and Electrical accessories in Ward No.06 , BBMP, Bangalore.
